

ID	ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
0	0		FDC Projects	1707 days?	6/15/16	12/29/22		45%	
1	1		Admin Building and WPSC 18-19 9292 Secure front Lobby and Cafeteria remodel @at admin/ Royal palm rooms and secure front lobby @ WPSC	452 days	8/14/18	7/1/20		39%	
2	2		Anona El 18-19 9250 Replace 15 Ton AC system media center	352 days	5/9/18	10/11/19		84%	
3	3		Anona ES. 19/20 10 Room Wing	835 days	3/1/18	8/13/21		13%	
4	4		Azalea MS 18-19 9294 Chiller Replacements	168 days	12/12/18	8/26/19		93%	
5	5		Bardmoor ES. 9106 Permanent walls	776 days	8/23/16	8/13/19		99%	
6	6		Bayside HS 18-19 9294 Chiller Replacements	182 days	12/12/18	9/13/19		92%	
7	7		Bear Creek ES 17-18 9280 Kitchen Hood/Electrical Distribution/ Lighting replacement	537 days	8/1/17	10/17/19		87%	
8	8		Bellair ES 18-19 9286 Seal, Coat and Striping	203 days	11/1/18	9/10/19		53%	
9	9		Bay Vista ES 18-19 9294 Chiller Replacement	179 days	12/12/18	9/10/19		92%	
10	10		Calvin Hunsinger 19-20 9332 Replace lighting throughout B1	395 days	5/8/19	12/16/20		4%	
11	11		Clearview Adult Learning Center 18-19 9604/0083 Roof replacement	220 days	3/27/19	2/19/20		51%	
12	12		Clearwater Fund 19-20 9338 4520 Upgrade Gym Flooring, Create Multipurpose room in Gym, Renovate Music Suite	352 days	5/8/19	10/9/20		6%	
13	13		Clearwater Hs 18-19 9251-4520 Major renovations/updates campus wide for academies and science labs	1171 days	3/12/18	12/29/22		26%	
14	14		Coil Replacements 18-19 9264	132 days	1/24/19	7/26/19		99%	
15	15		Countryside HS 18-19 4520 Remodel Science Labs Postponed for summer of 2020	566 days	5/9/18	9/4/20		66%	
16	16		Coachman Service Center 18-19 9308 New 10 Bay Facility	509 days	3/27/19	5/4/21		1%	
17	17		Curlew Creek ES 9104 New Parking	614.5 days	1/2/17	7/17/19		83%	
18	18		Cypress Woods El. 9174 12 Room wing	732 days	11/14/18	10/16/19		80%	
19	19		Cross Bayou ES 19-20 9327 Roof replacement B1,2,5 and walkways	357 days	5/8/19	10/16/20		0%	
20	20		Dixie Hollins HS 9238 17-18 Walkway lighting	534 days	8/1/17	10/15/19		76%	
21	21		Dixie Hollins HS 9295 17-18 Exhaust Hood/Roof	555 days	7/5/17	10/17/19		75%	
22	22		East Lake HS 18-19 9255 Replace generator and feeders B7	341 days	5/9/18	9/26/19		80%	
23	23		East Lake HS and MS 18-19 9290 Seal, Coat and Striping	166 days	11/1/18	7/19/19		76%	
24	24		East Lake HS 19-20 9339 Replace Chillers	352 days	5/8/19	10/9/20		0%	
25	25		East Lake HS 19-20 9333 Replace all exterior lighting with LED entire campus	352 days	5/8/19	10/9/20		0%	
26	26		Fairmount Park ES 18-19 9294 Chiller Replacement	164 days	12/12/18	8/19/19		90%	
27	27		Garrison Jones ES 18-19 9298/1481 Parking Lot	263 days	2/8/19	3/12/20		18%	

Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
28	28		Gibbs HS 19-20 9334 Replace parking & perimeter lighting	352 days	5/8/19	10/9/20		0%	
29	29		Gulf Beaches ES 9300 18-19 New 6 Wing Bldg	840 days	3/1/18	8/20/21		13%	
30	30		Hamilton Disston 9343 Building Envelope	714 days	9/7/16	8/9/19		99%	
31	31		John Sexton ES 9268 18-19 New 6 Room Wing	835 days	3/1/18	8/13/21		13%	
32	32		Lakewood HS 9091 New Gym lobby, weight	748 days	9/28/16	10/4/19		92%	
33	33		Lakewood HS 18-19 9289 Seal, Coat and Striping	216 days	11/1/18	9/27/19		63%	
34	34		Lealman Ave El 9253 18-19 Renovate entire HVAC syst/FA replacement/ Sanitary replacement B1 & B2	618 days	5/9/18	10/18/20		60%	
35	35		Lealman Innovation Academy 4520 200 Meter Track	328 days	5/20/18	9/20/19		84%	
36	36		McMullen Booth ES 18-19 9294 Chiller Replacement	188 days	12/12/18	9/23/19		91%	
37	37		Madeira Beach Fund K-8 9116 Windows	699 days	9/1/16	8/2/19		98%	
38	38		Madeira Beach Fund 19-20 9324 Replace 2 chilled water AHU in Band and Chorus B14	411 days	5/8/19	1/21/21		3%	
39	39		Meadowlawn MS 18-19 9278 Window/Building envelope	567 days	8/9/18	12/14/20		20%	
40	40		Meadowlawn MS 18-19 9285 Seal, Coat and Striping	169 days	11/1/18	7/24/19		44%	
41	41		Meadowlawn MS 18-19 9294 Chiller Replacement	173 days	12/12/18	9/2/19		91%	
42	42		Melrose El 9089 New Facility	1047 days	6/15/16	8/3/20		79%	
43	43		Midtown Academy 9279 18-19 Bus Drive and Parking Lot Renovations	398 days	6/11/18	2/7/20		39%	
44	44		Morgan Fitzgerald MS 19-20 9331 Ceiling and lights throughout	827 days	7/15/19	11/30/22		0%	
45	45		Mount Vernon El 18-19 9257 Upgrade Panelboards and feeders	337 days	5/9/18	9/23/19		78%	
46	46		North Shore ES 9121 Office Renovation	718 days	9/30/16	9/9/19		95%	
47	47		North Shore ES 18-19 New 6 Wing Bldg	840 days	3/1/18	8/20/21		13%	
48	48		Northeast HS 19-20 4520 Renovation for Academies	711 days	5/9/18	4/23/21		17%	
49	49		Northeast HS 18-19 9293 Cooling Tower Replacement	209 days	12/12/18	10/22/19		82%	
50	50		Oakhurst ES 19-20 4520 Remodel end of wings to create classrooms	352 days	5/8/19	10/9/20		5%	
51	51		Orange Grove ES 9149 New 12 Room Wing	870 days	9/20/16	3/7/20		92%	
52	52		Orange Grove ES 9299 18-19 IP paging	141 days	2/11/19	9/3/19		69%	
53	53		Osceola Fund High 19/20 New 18 Room Bldg.	920.5 days	3/1/18	1/3/22		10%	
54	54		Ozona ES 19-20 9326 Replace gutters Throughout	247 days	5/8/19	5/15/20		0%	
55	55		Palm Harbor MS 9100 AHU, Exhaust Fans	647 days	12/14/16	8/12/19		92%	
56	56		Palm Harbor University HS 9297 Roof	655 days	1/19/17	9/30/19		87%	
57	57		Pasadena Fundamental ES 9301 New 6 room addition	840 days	3/1/18	8/20/21		13%	

Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
58	58		Pinellas Park ES. 9117 Replace Windows	704 days	9/7/16	7/25/19		99%	
59	59		Pinellas Park MS 9090 New Facility	987 days	8/24/16	7/21/20		75%	
60	60		Pinellas Tech College SP 9047 Power Distribution	687.5 days	10/6/16	8/1/19		99%	
61	61		Pinellas Tech College-SP 18-19 9258 Replace metal halide fixture	359 days	5/9/18	10/22/19		68%	
62	62		Pinellas Technical College- St Pete 9203 Creek Restroration	799 days	1/1/18	5/3/21		35%	
63	63		PTC ST. Pete 19-20 9323 Replace Chillers	352 days	5/8/19	10/9/20		4%	
64	64		Plumb El. 19/20 New 10 Room Wing	835 days	3/1/18	8/13/21		13%	
65	65		Ponce De Leon ES 18-19 9260 Renovate Bldgs 1 & 4 MOVED TO FY 21-22	1110 days	5/9/18	11/30/22		12%	
66	66		Richard O. Jacobson 9141 New Buildings Pending Re-Design Estimate Review	973.5 days	12/22/16	11/16/20		68%	
67	67		Safety Harbor MS 18-19 9291 Seal, Coat and Striping	166 days	11/1/18	7/19/19		76%	
68	68		Sanderlin ES 9266 New 6 room Wing	835 days	3/1/18	8/13/21		13%	
69	69		Sanders Exceptional 19-20 9321 Replace Chillers	352 days	5/8/19	10/9/20		0%	
70	70		Sandy Lane ES 9319 18-19 Remodel for arts magnet	444 days	1/1/19	10/23/20		24%	
71	71		Sandy Lane El 18-19 9306 IP PAGING	137 days	3/25/19	10/2/19		49%	
72	72		San Jose Elem General 19-20 9337 4520 Campus Renewal	536 days	11/1/18	2/5/21		8%	
73	73		Sawgrass Lake El. 19/20 New 10 Rm Wing	835 days	3/1/18	8/13/21		12%	
74	74		Seminole ES 9269 New 6 Room Addition	835 days	3/1/18	8/13/21		13%	
75	75		Seminole MS 18-19 9307 IP PAGING	137 days	3/20/19	10/2/19		49%	
76	76		Seminole HS 18-19 9256 Replace Emergency exit windows per SREF report Postponed to summer of 2020 WILL NEED ADDITIONAL FUNDS	577 days	5/9/18	9/21/20		57%	
77	77		Seventy Fourth St ES 17-18 Major Renovations	412 days	7/25/19	4/16/21		0%	
78	78		Shore Acres ES 9267 New 6 Room Addition	837 days	3/1/18	8/17/21		13%	
79	79		Starkey 18-19 9293 (2-125 ton Trane) Chiller replacement 18/19	210 days	12/12/18	10/22/19		82%	
80	80		St. Pete HS 9188 17-18 Major Renovations	1068 days	7/19/17	1/4/22		37%	
81	81		St. Pete HS 9304 18-19 New Track and Field	198 days	2/13/19	11/15/19		71%	
82	82		Tarpon Springs HS 9092 Band/Orchestra Rm	885 days	10/3/16	5/28/20		61%	
83	83		Tarpon HS 19-20 9322 Replace Chillers	352 days	5/8/19	10/9/20		0%	
84	84		Tomlinson Adult Center 9088 Re-roofing	763 days	1/24/17	3/9/20		63%	
85	85		Tyrone MS 18/19 Major Renovations	1171 days	3/12/18	12/29/22		26%	
86	86		Woodlawn EL 18-19 9254 Replace fire alarm system Summer of 2020	578 days	5/9/18	9/22/20		61%	

Project: FDC Projects.mpp
Date: 7/25/19


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
87	87		Westgate ES 19-20 9328 Reroof building and replace gutter and downspouts	327 days	5/8/19	9/4/20		0%	
88	88		WPSC 9296 18-19 Electrical Distribution/ New service entrance for shops and Transportation	366 days	1/23/19	7/23/20		56%	
89	89		PCSB-YMCA Partnership School	656 days	5/23/19	2/11/22		0%	
95	95		z04 Complete						
96	96		z05 Closeout/Reconciliation						
97	97		z06 On hold or Cancel						
98	98		z07 Bonding Projects-Issue #1						
99	99		z08 Bonding Projects-Issue #2 18/19						
100	100		z09 Bonding Projects-Issue #3 19/20						




Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

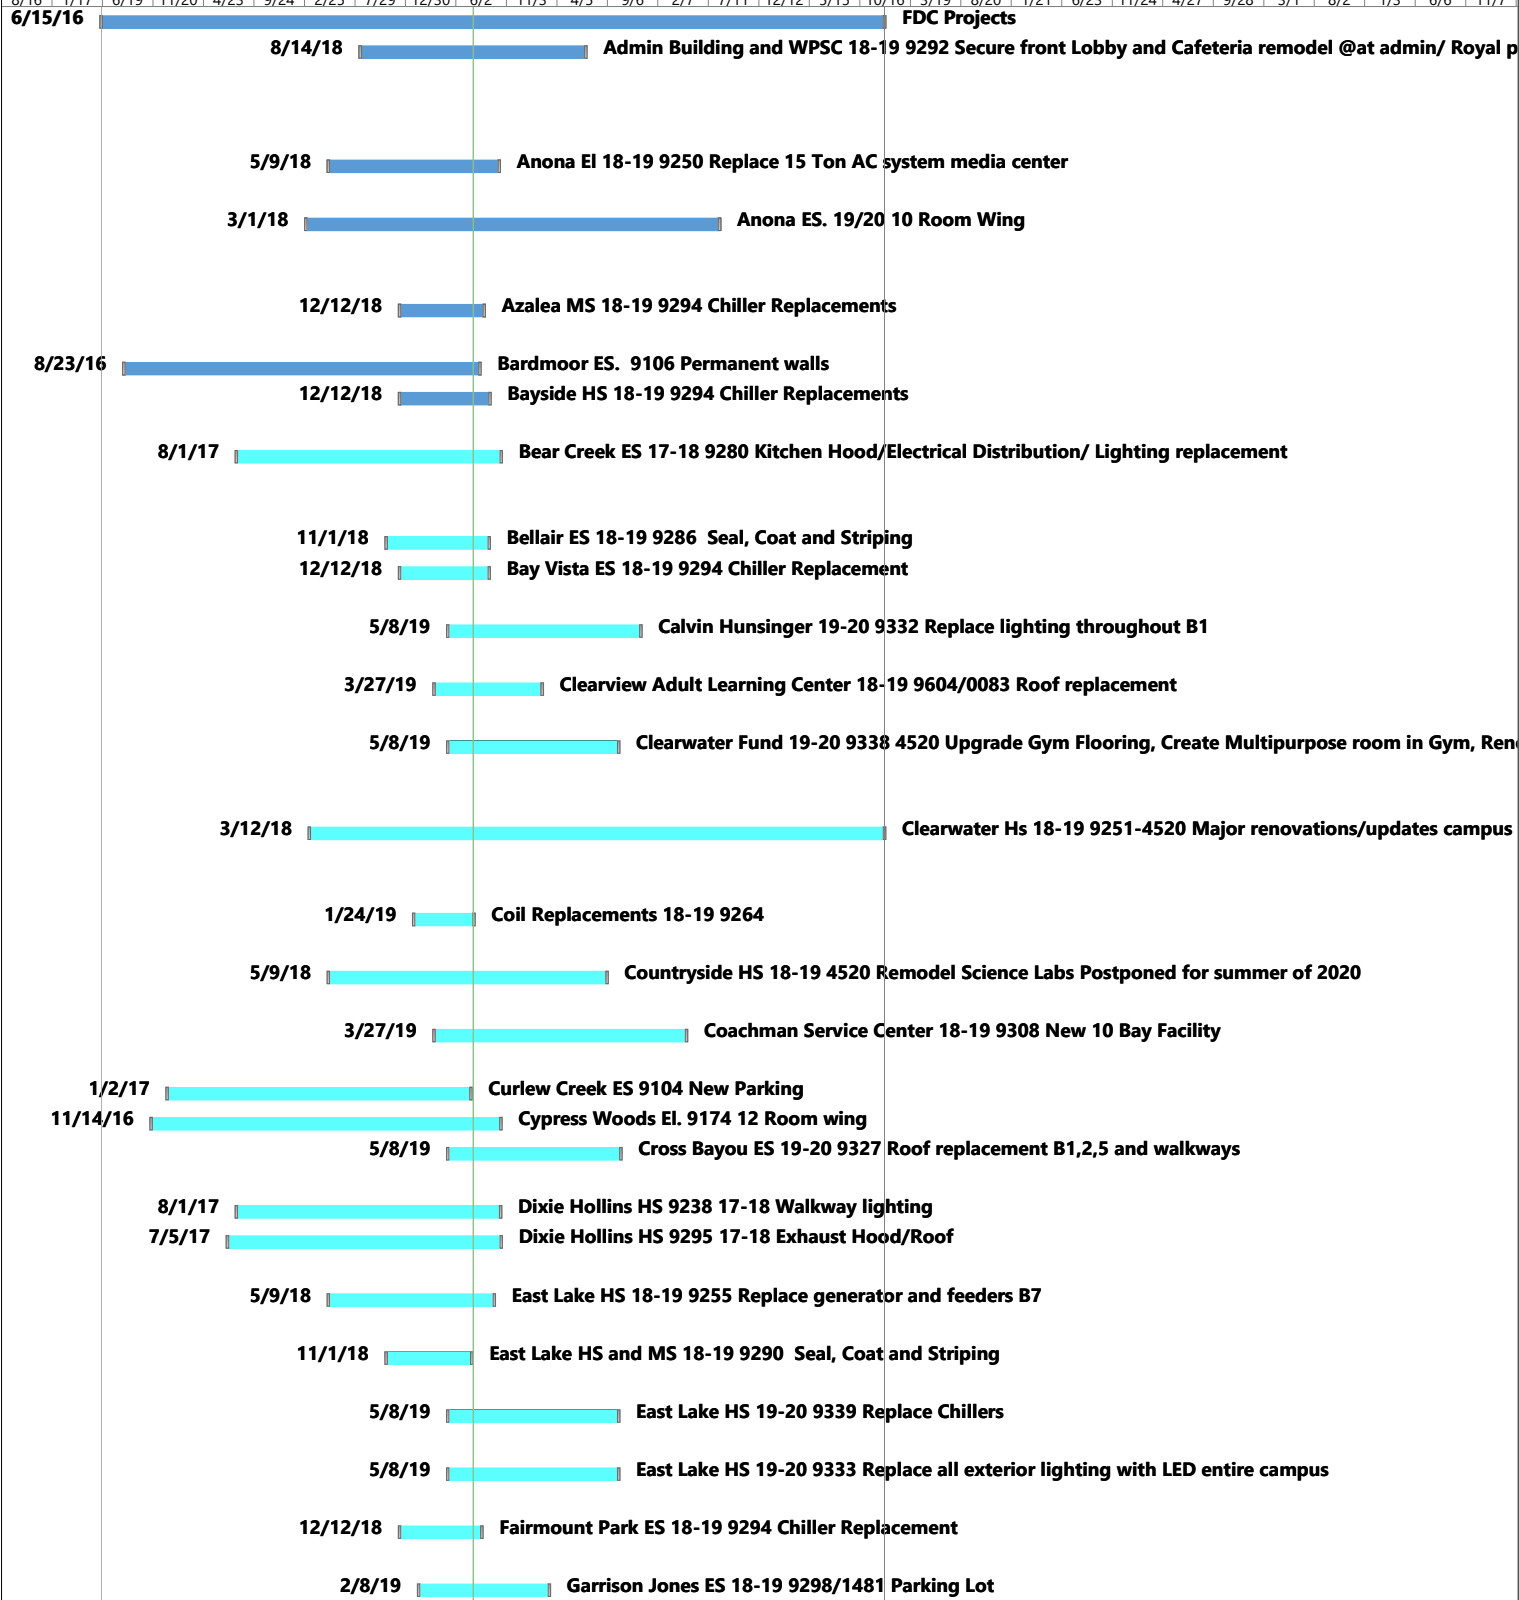


Project: FDC Projects.mpp
 Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

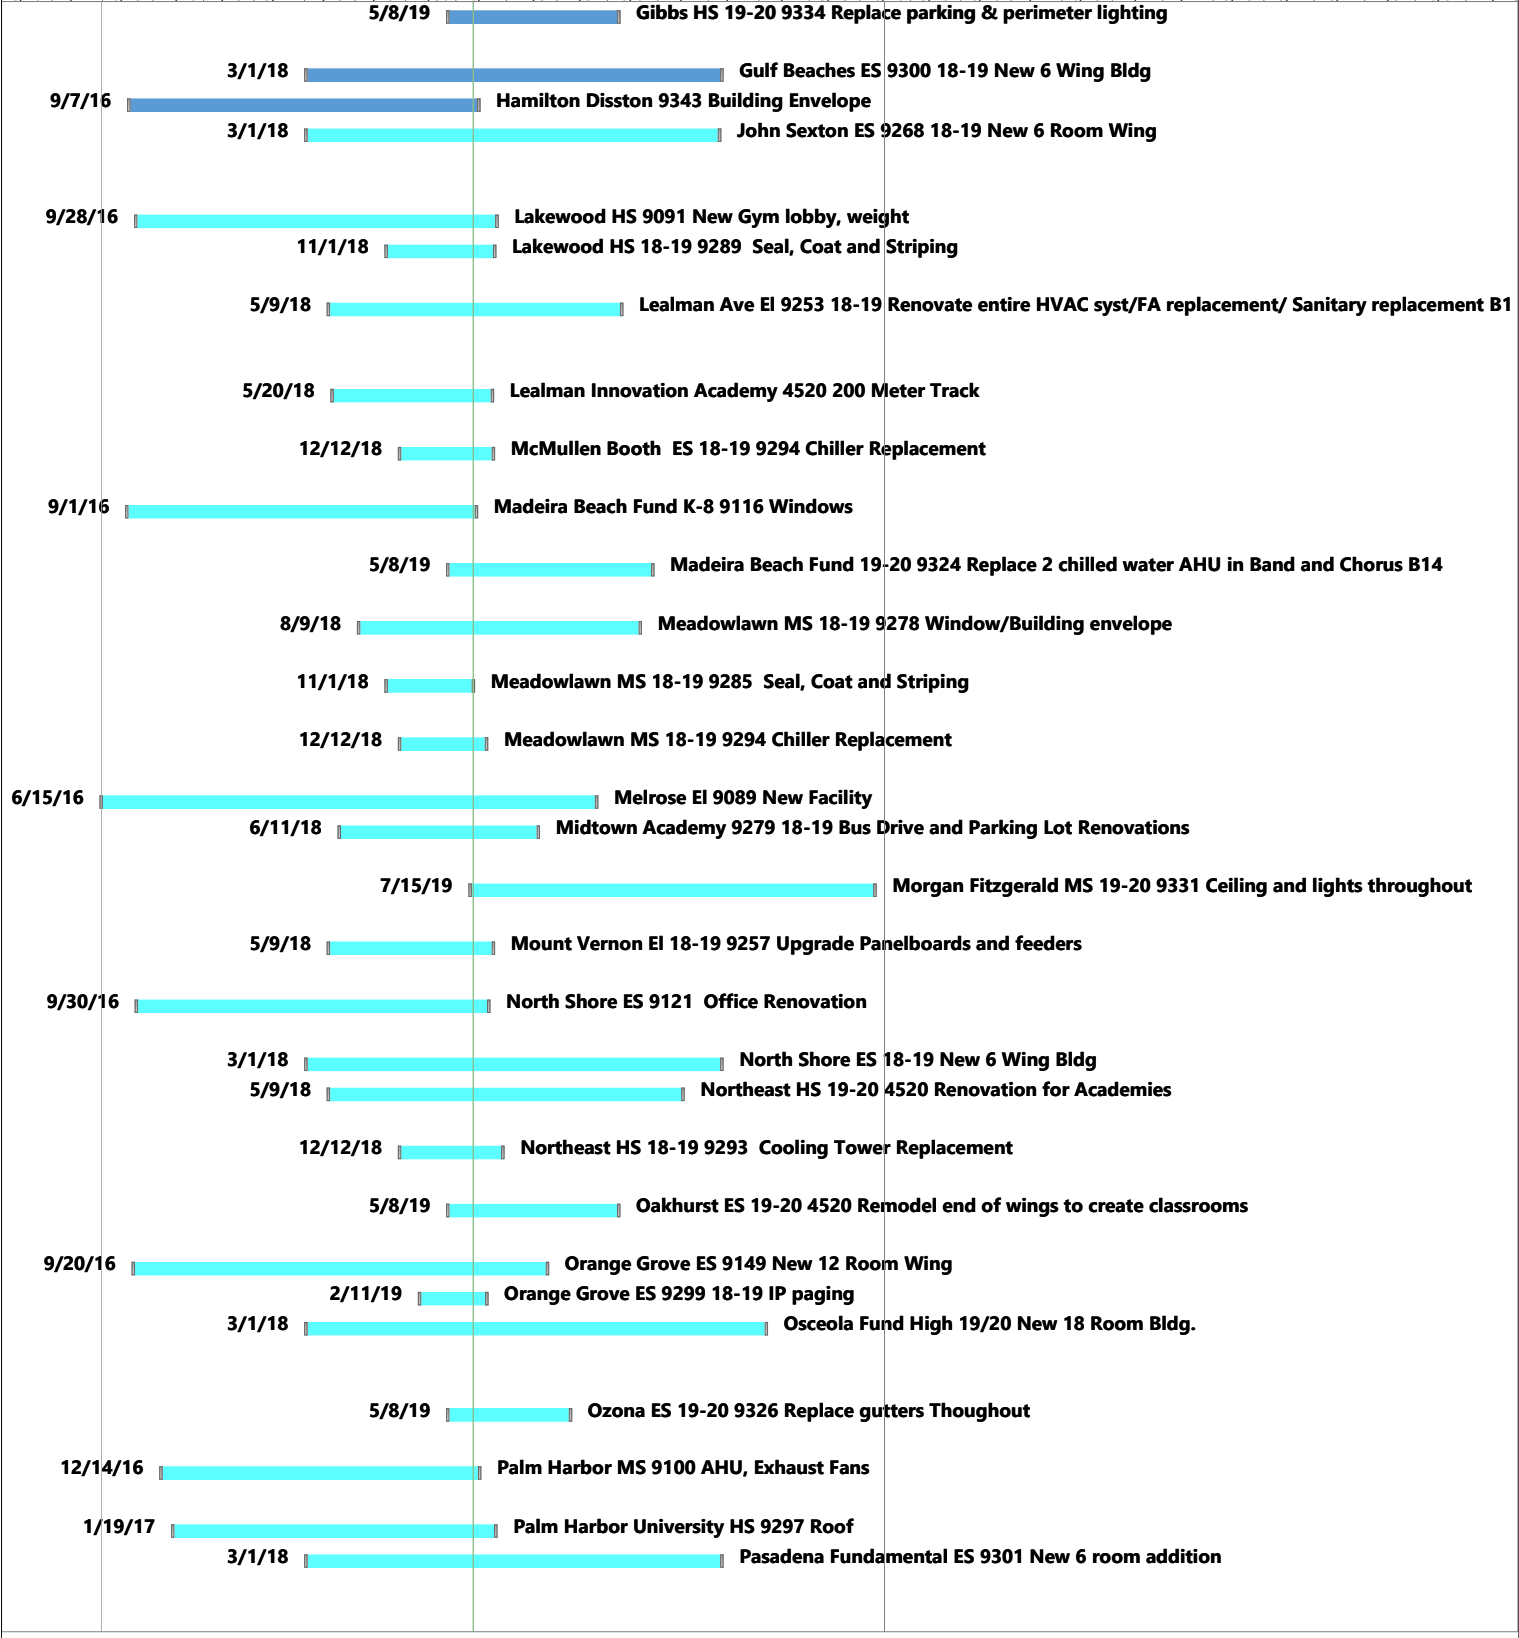


Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

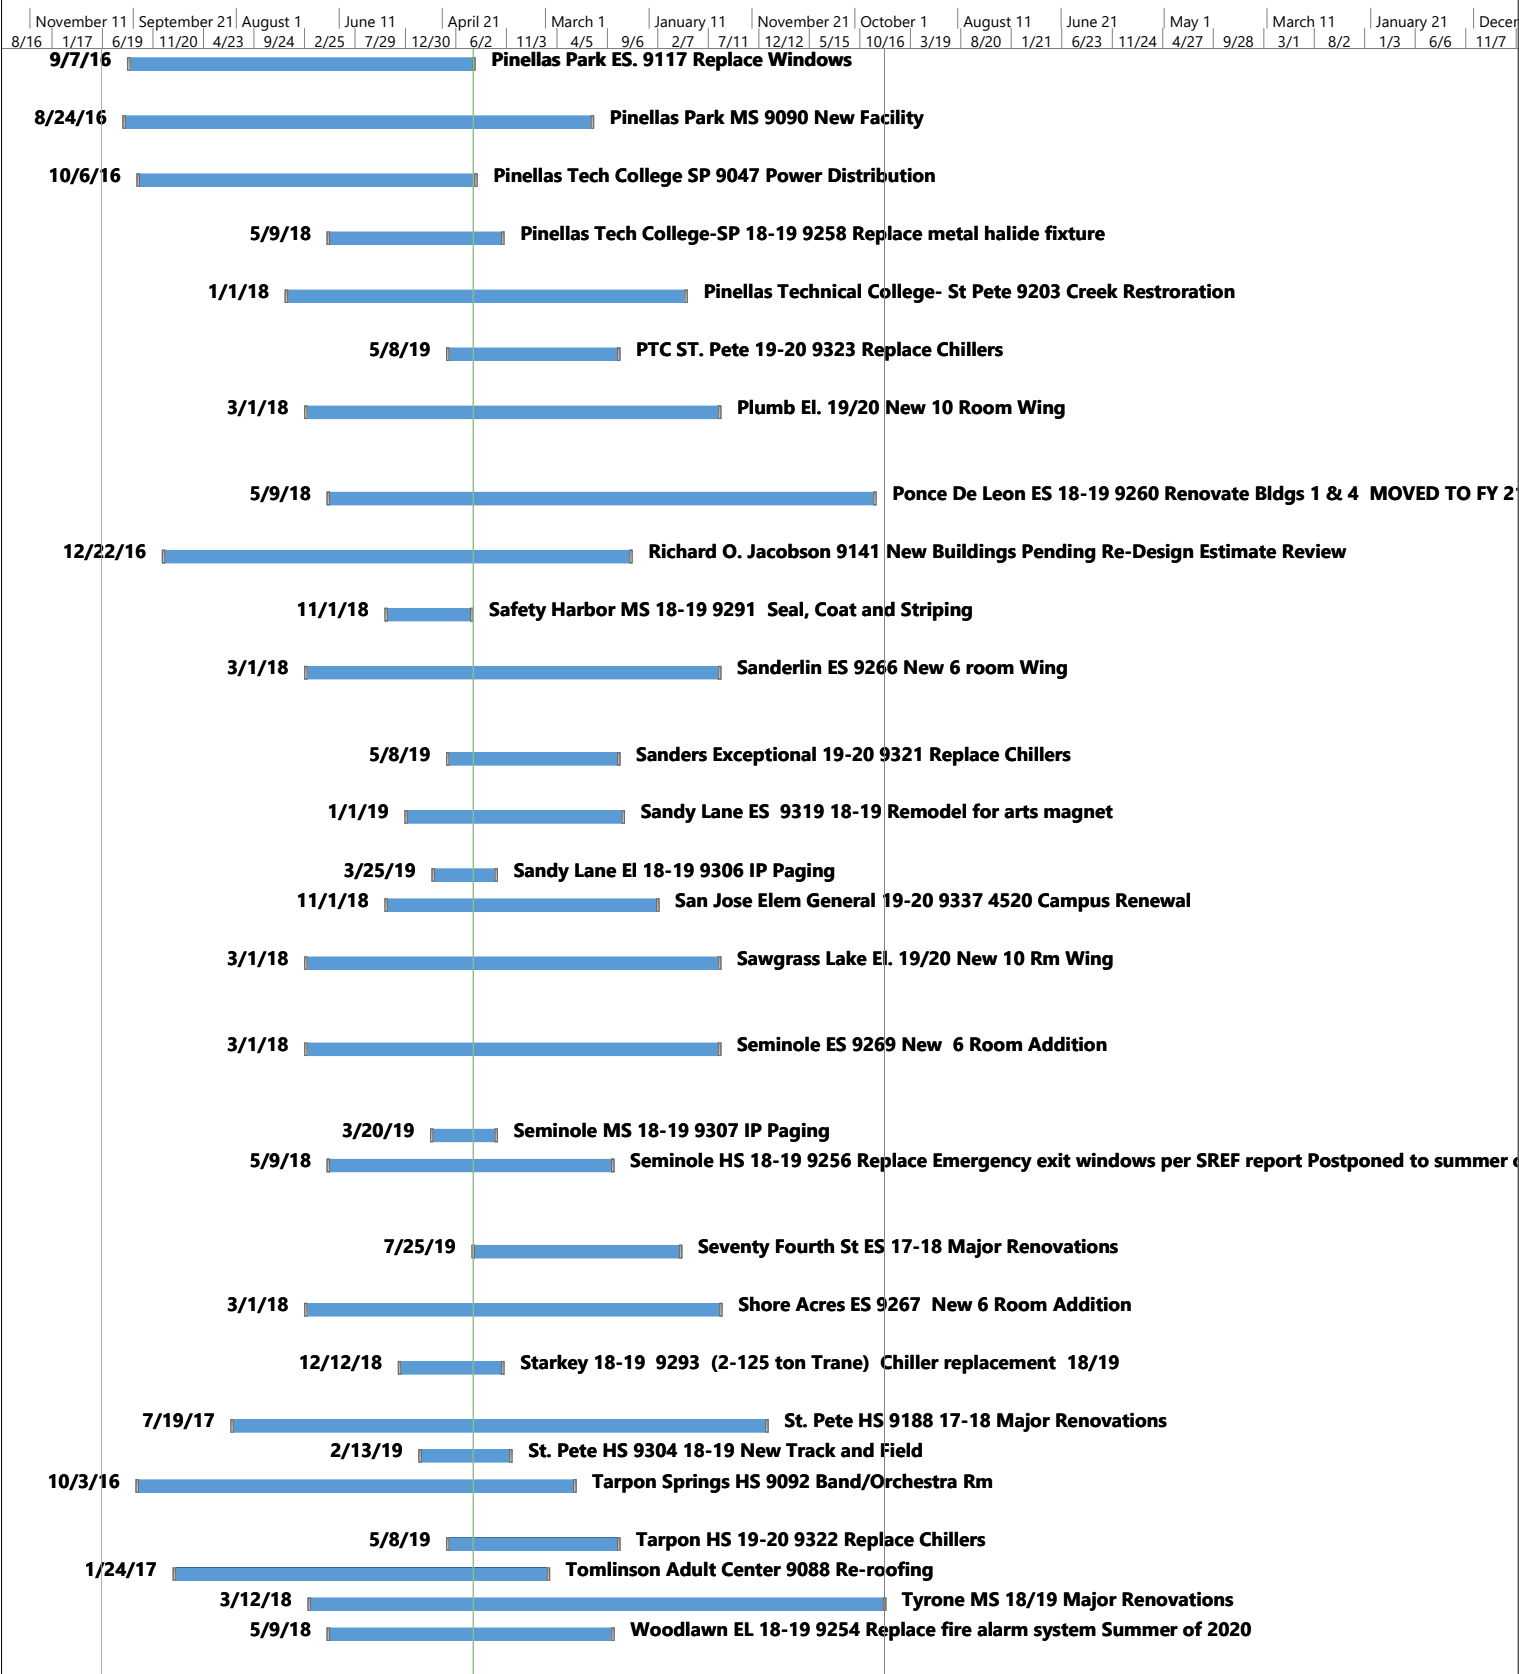

Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

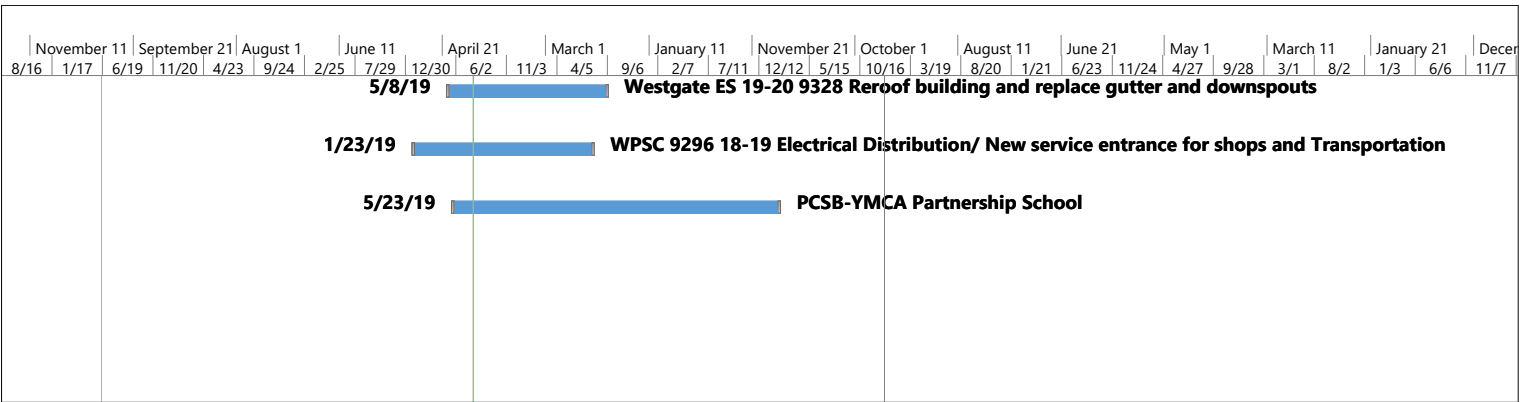

Project: FDC Projects.mpp
Date: 7/25/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
